
TEST CERTIFICATE FOR DYNAFLUX AC INDUCTION WORM GEARED MOTOR

DD/F/05

Purchaser **B.N. ENTERPRISES**
SR NO. 44/9, NARHE INDUSTRIAL ESTATE,
NEAR PARY COMPANY, NAHREGAO,

MFD. By = **MMC Electric Company Pvt. Ltd.**
Plot No.154, S.No 585,
Machhe Industrial Estate,Machhe,
MACHHE BELGAUM-590 014, KARNATAKA, INDIA

Certificate No : MMCB/20222023/IS-IS01/000046 **Order No** : 7 04/05/2022
POWER\TORQUE : 0.5HP **SPEED** : 1330RPM **VOLTAGE** : 415VAC 3PH **MOUNTING** : FLANGE(B5)
CONST. : TEFC **INSULATION CLASS** : F **DRAWING NO.** : MI-AC/71B5-M(040)FT **OUTPUT SPEED** : 46RPM
PARTY DRAWING NO. :

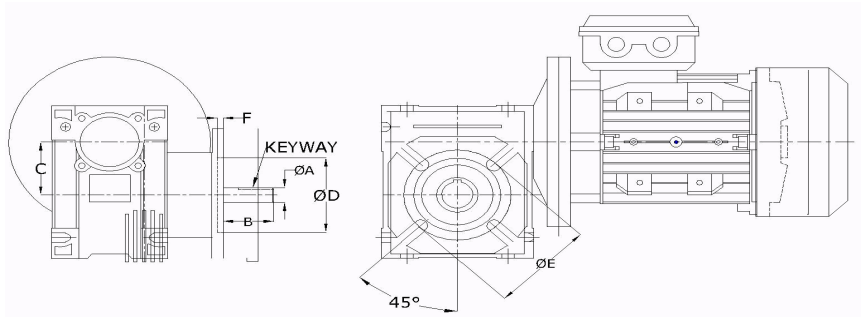

	A	B	C	D	E	F	G	H	I	J	K
052201571	18.0				75						

ELECTRICAL CHECKING											
	NO LOAD					FULL LOAD					
KEYWAY	VOLTAGE (A.C.)	SPEED (R.P.M.)	CURRENT (AMPS.)	TEMPERATURE (°C)		VOLTAGE (A.C.)	SPEED (R.P.M.)	CURRENT (AMPS.)	TEMPERATURE (°C)	HV = 1.5 KV	VIBRATION INTENSITY Double Amplitude in Microns
	415	50	0.76	25		415	46	1.4	38	OK	05

1) Momentary overload test for 20 seconds at 50 % of full Load : Yes
2) Special Features : (if any) =

Certified that the motor has been found electrically and mechanically sound and in working order in all respects. Futher Certified that the motor has passed all routine tests and complies with governing specifications.

Tested By :- Satish Halgekar Tested Date :- 28/05/2022


TEST CERTIFICATE FOR DYNAFLUX AC INDUCTION WORM GEARED MOTOR

DD/F/05

Purchaser **B.N. ENTERPRISES**
SR NO. 44/9, NARHE INDUSTRIAL ESTATE,
NEAR PARY COMPANY, NAHREGAO,

MFD. By = **MMC Electric Company Pvt. Ltd.**
Plot No.154, S.No 585,
Machhe Industrial Estate,Machhe,
MACHHE BELGAUM-590 014, KARNATAKA, INDIA

Certificate No : MMCB/20222023/IS-IS01/000047 **Order No** : 7 04/05/2022
POWER\TORQUE : 2.0HP **SPEED** : 1380RPM **VOLTAGE** : 415VAC 3PH **MOUNTING** : FLANGE(B5)
CONST. : TEFC **INSULATION CLASS** : F **DRAWING NO.** : MI-AC/90B5-M.(090)FL **OUTPUT SPEED** : 23RPM
PARTY DRAWING NO. :

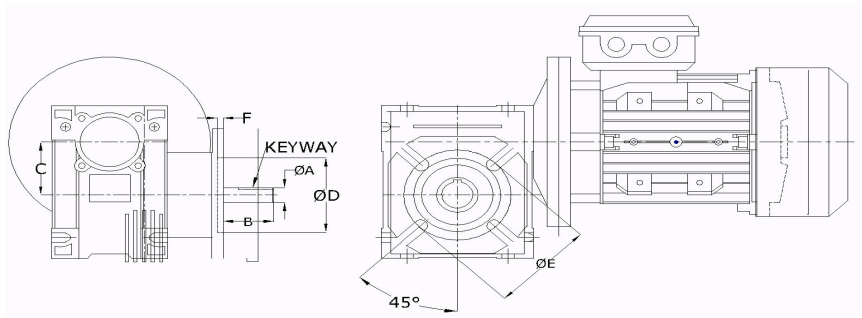

	A	B	C	D	E	F	G	H	I	J	K
052201572	35.0			152	175	6					

ELECTRICAL CHECKING											
	NO LOAD					FULL LOAD					
KEYWAY	VOLTAGE (A.C.)	SPEED (R.P.M.)	CURRENT (AMPS.)	TEMPERATURE (°C)		VOLTAGE (A.C.)	SPEED (R.P.M.)	CURRENT (AMPS.)	TEMPERATURE (°C)	HV = 1.5 KV	VIBRATION INTENSITY Double Amplitude in Microns
	415	25	2.0	25		415	23	3.8	40	OK	06

1) Momentary overload test for 20 seconds at 50 % of full Load : Yes
2) Special Features : (if any) =

Certified that the motor has been found electrically and mechanically sound and in working order in all respects. Futher Certified that the motor has passed all routine tests and complies with governing specifications.

Tested By :- Satish Halgekar Tested Date :- 28/05/2022
