SGS



IITB - MONASH RESEARCH ACADEMY

IIT POWAI - MUMBAI

MONTHLY PROGRESS REPORT

OCTOBER 2013

SGS

IITB MONASH RESEARCH ACADEMY

IIT POWAI, MUMBAI- 400076

CONTENTS

1	PROJECT BRIEF AND PARTICIPANTS.
2	WORK AWARD STATUS.
3	PROJECT TRACKER.
4	BUDGETARY WORK PROGRESS DATA.
5	WORK PROGRESS STATUS (COST WISE).
6	CUMULATIVE WORK STATUS.
7	HIGHLIGHTS OF THE MONTH.
8	QUALITY ASSURANCE.
9	SAFETY REPORT.
10	ACTION AND ISSUE TRACKER.
11	DESIGN & DRAWING UPDATE.
12	DEPLOYMENT.
13	MATERIAL PROCUREMENT.
14	PROJECT DIRECTORY.
15	PROJECT PHOTOGRAPHS.

Prepared By- Amit S Pawar **Approved By- R N Tanna**

SGS

PROJECT BRIEF & PARTICIPANTS

REPORT DATE- 1st November 2013



IITB MONASH RESEARCH ACADEMY

REPORT NO.	**SGS/ IND/ MUM/ IITB/ FPR/ 005/ 2013**
FILE. NO.	**IN/ MUM/ IND/ 201300378/ 005**
PROJECT NAME	**IITB MONASH RESEARCH ACADEMY**
CLIENT NAME	**IITB MONASH**
PMC	**SGS INDIA PVT. LTD.**
ARCHITECTS	**VENKATARAMANAN ASSOCIATES**
RCC CONSULTANTS	**STRUDCOM CONSULTANTS PVT. LTD**
PHE CONSULTANTS	**ACE CONSULTANTS**
ELECTRICAL CONSULTANTS	**ABHIYANTA ELEC. CONS. & ENGRS.**
HVAC CONSULTANTS	**R . S . KULKARNI**
CONTRACTOR	**GOLANI BROTHERS**
PROJECT DURATION- FROM/ TO	**01ST AUGUST 2013 TO 31ST MARCH 2015**
LOCATION	**IIT BOMBAY, POWAI.**
TYPE OF PROJECT	**G +3 INSTITUTIONAL**
PROPOSED BUILT UP AREA	**60,000 SQFT. (APPROX)**
CONTRACT REF. NO	**LOI OF IITB DATED 1ST MARCH 2013.**
Prepared by: **AMIT S. PAWAR**	Approved by: **RAJU N. TANNA**

WORK AWARD STATUS

S NO	WORK PACKAGE	NAME OF AGENCY	DATE OF AWARD OF WORK	VALUE OF WORK AWARDED	REMARKS
1	Civil Works	Golani Bros.	20.06.13	132,242,747.00	Contract issued to contractor dated. 20th June 2013.
2	PHE Works	"		6,782,419.00	
3	Electrical Works	"		18,312,248.00	
4	Fire Fighting System	"		1,217,970.00	
5	HVAC	"		40,922,901.00	
6	Fire Alarms System	"		4,487,400.00	
7	Lift	"		4,093,287.00	
8	ADDEDUM- supplementary item	"		19,663,806.00	
			TOTAL VALUE OF WORK =	**227,722,778.00**	

Prepared By- AMIT S PAWAR **Approved By- RAJU N TANNA**

SGS

MONASH RESEARCH ACADEMY, IITB POWAI.

	Baseline Sart date: 01/08/2013		Baseline Finish date: 30/03/2015		Total Duration of Project (days): 600					
Sr No	Work Package	Duration of work (days)	Scheduled Start date	Scheduled Finish date	Actual Start Date	Total Delay in Actual start	Actual Finish Date	Total Delay in Actual finish	Approved Hindrance (days)	Remark.
A	SUB STRUCTURE- CIVIL	180	01 August 2013	31 January 2014	13 August 2013				14 days	-
1	Excavation	75	01 August 2013	15 October 2013	13 August 2013	13 days	15 October 2013	0 days	13 days	* -Refer Hindrance register for more details.
2	PCC for footing	68	16 August 2013	23 October 2013	27 August 2013	11 days	18 October 2013	0 days	-	Finished 4 days before schedule.
3	Water Proofing U.G.Tank / Lift (1) & (2)	60	24 August 2013	23 October 2013	28 September 2013	34 days	In Progress			Started 35 days late. (Waterproofing for UG Tank balance.)
4	Formwork for footing	68	24 August 2013	31 October 2013	28 August 2013	4 days	23 October 2013	0 days	-	Finished 7 days before schedule.
5	Reinforcement work	64	31 August 2013	10 November 2013	29 August 2013	-	19 October 2013	-	-	Finished 19 days before schedule.
6	Concreting of footing	68	07 September 2013	26 November 2013	05 September 2013	-	23 October 2013	-	1 day	Finished 33 days before schedule.
7	Plum Concrete	8	22 September 2013	30 September 2013	28 October 2013	36 days	In Progress			Started 36 days late.
8	Stub Column	68	15 September 2013	23 November 2013	24 September 2013	9 days	29 October 2013	35 days	-	Started 9 days late.
9	Formwork / reinforcement for lift, wall, U.G Tank & Concrete FOR U.G.W.T Wall & Lift	60	30 September 2013	29 November 2013	03 October 2013	3 days	In Progress	-	-	Started 3 days late.
10	Backfilling	75	23 September 2013	07 December 2013	16 September 2013	-	In Progress	-	-	Started 7 days before schedule.
11	Plinth Beam works	75	17 October 2013	31 December 2013	21 October 2013	4 days	In Progress			Started 4 days late.
12	Brickwork upto plinth/ Plinth filling and compaction	60	16 November 2013	15 January 2014						-
13	Soiling / ATT	45	09 December 2013	23 January 2014						-
14	PCC for flooring	30	01 January 2014	31 January 2014						-
										-
B	SUPERSTRUCTURE-CIVIL	240	03 December 2013	31 July 2014						
C	GENERAL FINISHES	390	31 January 2014	28 February 2015						-
D	PLUMBING AND FIRE	262	06 June 2014	23 February 2015						-
E	ELECTRIC WORKS	465	15 November 2013	24 February 2015						-
										-

SGS

MONASH RESEARCH ACADEMY, IITB POWAI.

	Baseline Sart date: 01/08/2013		Baseline Finish date: 30/03/2015		Total Duration of Project (days): 600					
Sr No	Work Package	Duration of work (days)	Scheduled Start date	Scheduled Finish date	Actual Start Date	Total Delay in Actual start	Actual Finish Date	Total Delay in Actual finish	Approved Hindrance (days)	Remark.
F	HVAC WORKS	360	05 March 2014	28 February 2015						-
G	IBMS	150	01 October 2014	28 February 2015						-
H	LIFT WORK	210	02 August 2014	28 February 2015						-
I	FINAL TESTING/ FINISHING &	60	30 January 2015	31 March 2015						-
	Total Cost of Project (In Rs,)									

Prepared by: R N TANNA

SGS


ITEM WORK PROGRESS UPDATE

Sr. No.	Work Package	% Cost of item	Unit of Item/ Sub Item	Qty. as per BOQ	Qty. completed as on date	Qty. completed in %	Cost of Item in INR	Remark.
A	**SUB STRUCTURE- CIVIL**	**10.49%**	**-**	**-**	**-**	**-**	**23,880,000.00**	**-**
1	Excavation in soil (upto 1.5m)	-	cu.m	688.00	**1177.00**	**171.08%**	-	Actual Quantity Exceeded BOQ Qty.
2	Excavation in soft rock (1.5 - 3m)	-	cu.m	275.00	**1147.00**	**417.09%**	-	"
3	Excavation in hard rock	-	cu.m	160.00	**1.46**	**0.91%**	-	Actual Qty. reduced as no hard rock encountered.
4	PCC for footing	-	cu.m	109.00	117.70	107.98%	-	"
5	Water Proofing U.G.Tank / Lift (1) & (2)	-	sq.m	175.00	169.04	96.59%	-	-
6	Formwork for footings	-	sq.m	1090.00	824.40	75.63%	-	-
7	Reinforcement work	-	MT	148.00	42.00	28.38%	-	-
8	Concrete for footings, lift rafts M:25	-	cu.m	729.00	728.24	99.90%	-	-
9	Concreting of plinth beams, stub column, lift pardis etc. M:40	-	cu.m	570.00	51.00	8.95%	-	-
10	Plum Concrete	-	cu.m	22.00	**55.00**	**250.00%**	-	Actual Quantity Exceeded BOQ Qty.
11	UG TANK/ Lift / Stub Column shuttering	-	sq.m	440.00	169.60	38.55%	-	-
12	Plinth Beam shuttering	-	sq.m	789.00	165.00	20.91%	-	-
13	Backfilling in plinth	-	cu.m	450.00	0.00	0.00%	-	-
14	Soiling	-	sq.m	1725.00	0.00	0.00%	-	-
15	ATT	-	sq.m	1725.00	0.00	0.00%	-	-
16	PCC for flooring	-	sq.m	287.00	0.00	0.00%	-	-
B	**SUPERSTRUCTURE- CIVIL**	**22.39%**					**50,996,174.00**	**-**
C	**GENERAL FINISHES**	**33.82%**					**77,013,262.77**	**-**
D	**PLUMBING AND FIRE FIGHTING**	**3.51%**					**7,993,069.00**	**-**
E	**Electric Works**	**8.04%**					**18,312,062.48**	**-**
F	**HVAC WORKS**	**17.97%**					**40,921,783.03**	**-**
G	**IBMS**	**1.97%**					**4,487,015.31**	**-**
H	**LIFT WORK**	**1.81%**					**4,115,014.04**	**-**
I	**FINAL TESTING/ FINISHING &**	**0.00%**					**0.00**	**-**
	TOTAL COST	**100%**					**227,722,777.00**	

Prepared By:- AMIT S. PAWAR **Approved By:- RAJU N. TANNA**

SGS

ITEM PROGRESS STATUS CHART

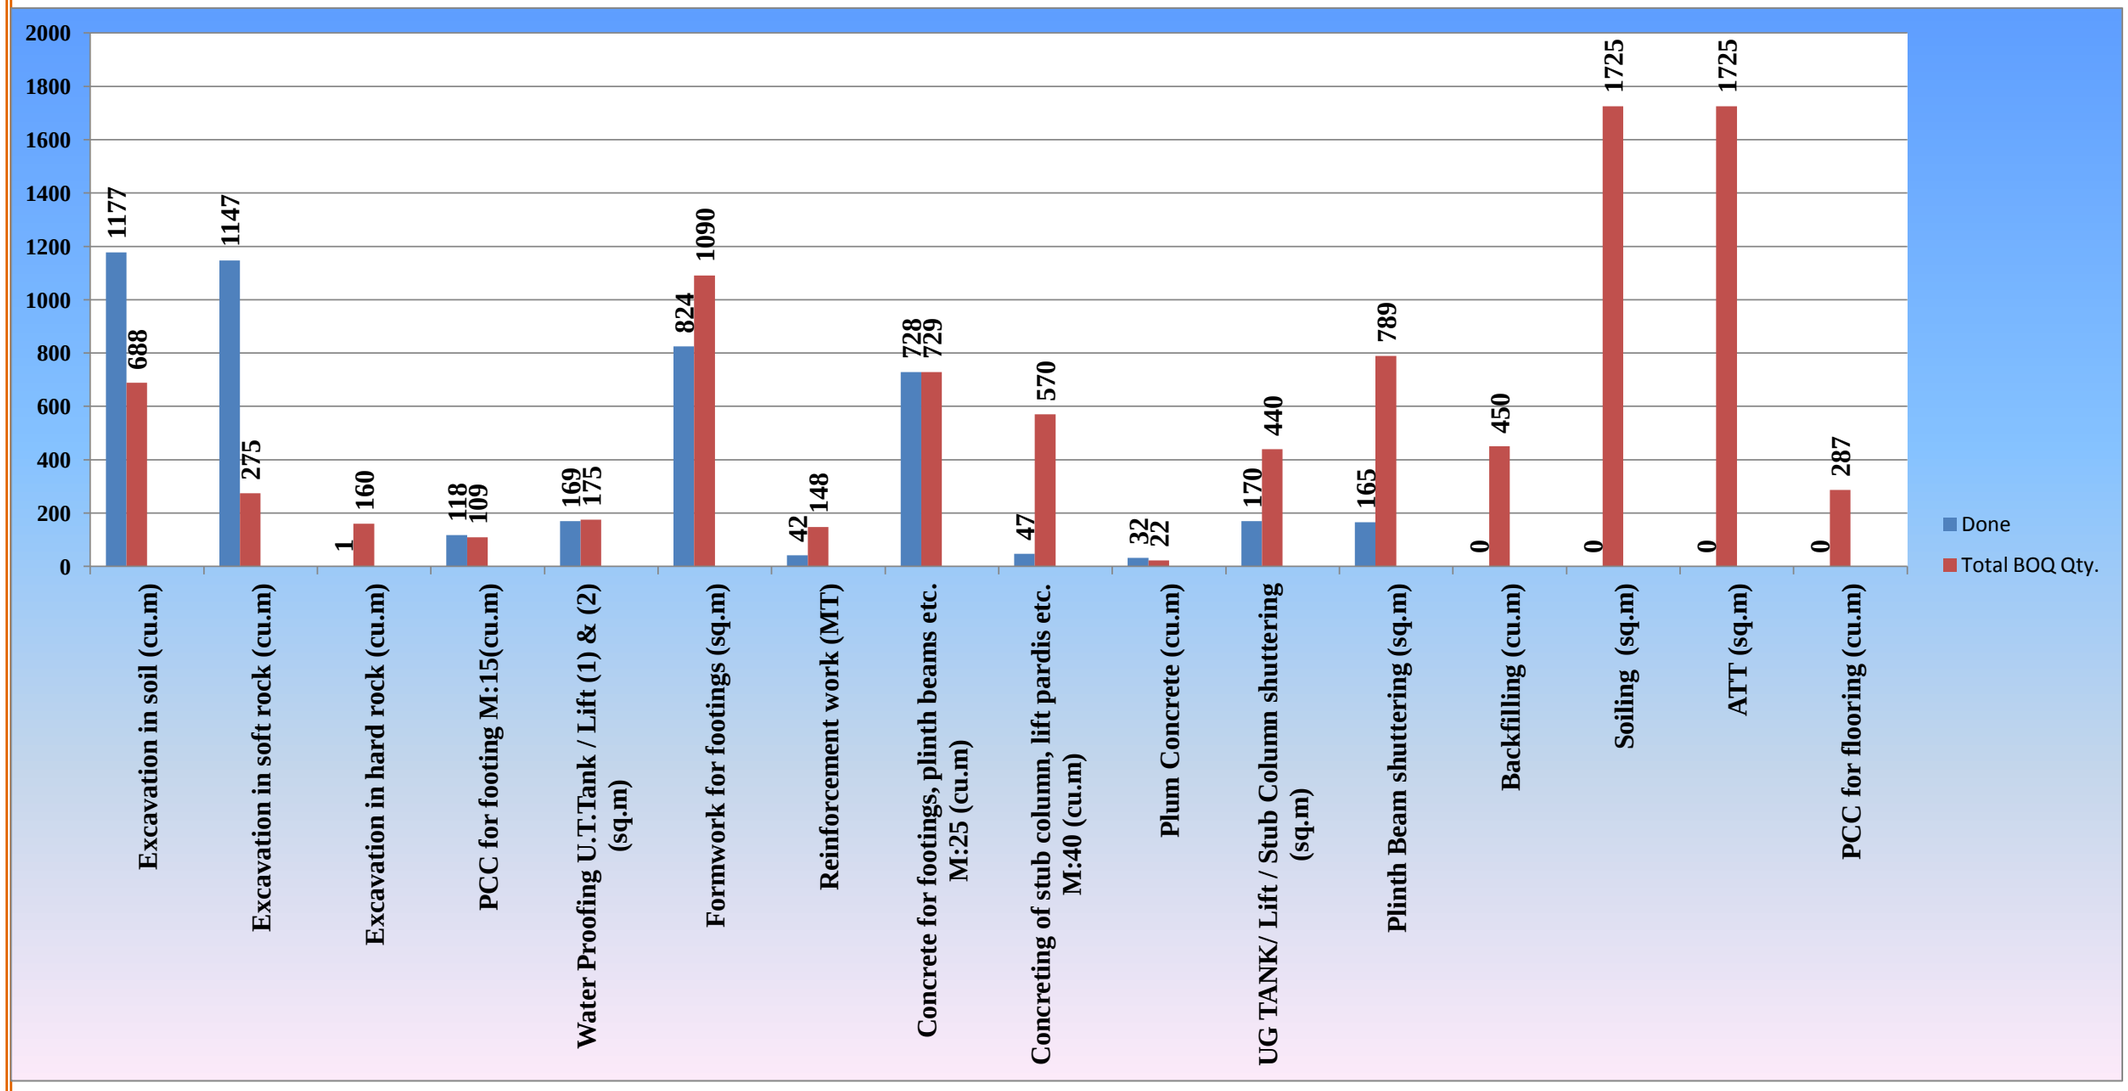

Prepared By- AMIT S PAWAR

Approved By- RAJU N TANNA

SGS

DETAILS OF PAYMENT

Sr. No.	Payment against	Period of Work Done	Date of Submission of claim by Golani Bros.	Amount Claimed	Total Recovery	Amount Certified	Payment Done	Date of Payment	Remarks
1	Mobilisation Advance	-	19-Aug-13	25,000,000.00	0.00	0.00	25,000,000.00	3-Sep-13	Clause -10B(ii) of Tender Contract.
2	1st R.A	Aug-13	16-Sep-13	7,961,521.98	530,861.00	7,430,660.98	7,433,651.00	27-Sep-13	1) For recovery details please refer Recovery statement of certified bill.
3	-	-	-	-	-	-	-	-	2) For Amount Paid- Refer RA-1 certificate from IITB
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
	-	-	-	-	-	-	-	-	
Prepeared By- AMIT S PAWAR								**Approved By- RAJU N TANNA**	

SGS

HIGHLIGHTS OF LAST 30 DAYS

Sr. No.	Description	Remarks
1	100% Excavation work completed. All Column footings, Lift shafts in sub structure, stub columns upto plinth beam bottom completed. Backfilling around footings completed. Compaction done.	Execution Progress status.
2	Waterproofing for LIFT-1 & LIFT-2 done below raft, vertical sides of rafts, raft tops, shaft pardis in sub structure.	Completed for substructure.
3	U G Tank works (plum concrete) commenced on 25th October and is in progress.	Revised Drg. Recd. Dated.09.10.13
4	Dean IPS had done correspondence with Monash relating to effluent types and disposal dated.10th October & with VA dated. 15th October.	By Mail & tel .discussion respectively.
5	Effluent disposal system discussed between SGS,VA & IITB in joint meeting on 29th October. For details refer MOM-022 dated 29.10.13	VA to design the drainage system accordingly and release GFC working drawings.
6	Clarification for addition of four columns. C149 to 152 given by VA.	Clarification received by mail. Dated. 4th October
7	Discrepancy in Chord sections notified to VA by SGS dated.7th October.	Clarification received by mail. Dated. 8th October
8	Discrepancy in FAS were sent to VA by SGS.	Clarification received dated. 11th October from VA.
9	Clarification on water supply line layout given by VA dated. 8th October.	Clarifiaction received by mail. Revised layout GFC drgs.awaited.
10	Discrepancy in FF drawings forwarded to VA by SGS dated. 7th October.	Clarification received dated. 19th October from VA.
11	Requirement for drainage layout through labstore, washroom, AHU on the ground floor forwarded to VA by SGS dated 8th October.	Revised GFC Drg. Awaited.
12	5 Weekly review meeting conducted during October month, Details in MOM- 018, 019, 020, 021, 022 forwarded to IITB and all concerned.	-
13	Monthly Progress Report for September 2013, (MPR-004) hard copy submitted & Fortnight Progress Report (005)- 1st to 15th October soft copy given to to IITB by SGS.	-
14	Floorwise Effluent point details submitted to IITB by SGS.	-
15	List of Pending Drgs. Mail sent to VA dated. 17th October & delivery schedule of drgs./ reply received from VA dated.19th October.	Reply from VA recd. 19th October
16	Plinth Beam compaction and PCC started on 19th October. Work in progress.	Execution Progress status.
18	All Columns Footings casting completed on 23rd October 2013.	Execution Progress status.
19	Anti Termite Treatment around columns did not commence.	Execution Progress status.
20	Site levelling upto Natural Ground level completed.	Execution Progress status.
21	Mr. Pritam & Mrs. Namrata (Sr. Architects, VA) visited the site on 29th October 2013, Inspection Report of site visit to be sent by VA.	-
22	2 Safety TBT conducted on site by SGS. For details refer TBT- 008 & 009 sent to all concerned.	-
23	Plinth Beam casting is in progress.	Execution Progress status.

Prepared By:- AMIT S. PAWAR **Approved By:- RAJU N TANNA**

SGS

ACTION POINT FOR NEXT 30 DAYS

Sr. No.	Description	Remarks
1	Plinth Beam casting completion.	-
2	UG Tank construction to complete for substructure(First lift).	-
3	ATT around columns to complete in substructure.	-
4	Issue of Effluent Drainage layout GFC drawings.	Expected from VA.
5	Review & proof checking of PT Slab design.	Golani Bros. to follow up.
6	Clearance of Slab casting methodolgy approval from Strudcom.	Golani Bros. to follow up.
7	Submission of RA-2 by Golani Bros.	-
8	Submission of Monthly supervision bill by SGS.	-
9	Plinth filling, PCC & commencement of superstructure works.	-
10	-	-
11	-	-
12	-	-
13	-	-
14	-	-
15	-	-
16	-	-
17	-	-
18	-	-
19	-	-
20	-	-

Prepared By:- **AMIT S. PAWAR** **Approved By:-** **RAJU N TANNA**

SGS

QUALITY ASSURANCE PLAN

Sr. No.	Material / Activity	Makes of Material	Whether Appoved	Quantity Received to date	No. of tests to be carried out.	Actual tests done at Site/Lab		Results Specify	Remarks
						Site Lab	Outside Lab		
Material (CIVIL)									
1	Steel-Fe 500 D	MITC	YES	148.6	0	0	Refer Remarks	OK	1 per specimen per lot, each for physical & chemical properties tested. Copy of result submitted to IITB.
2	RMC (M15)	Godrej & Boyce	YES	163.25	27	27	0	OK	-
3	RMC (M25)	Godrej & Boyce	YES	712.50	193	193	0	OK	
4	RMC (M40)	Godrej & Boyce	YES	79.50	27	27	-	OK	-
5	Soil (Proctor Density Test)	-	-	-	-	-	-	-	**Results awaited from Strucwel.**
Material (MEP)									
-	-	-	-	-	-	-	-	-	-
-	-	-	-	-	-	-	-	-	-
Agency Approval									
-	-	-	-	-	-	-	-	-	-
-	-	-	-	-	-	-	-	-	-

Prepared By:- **AMIT S. PAWAR** **Approved By:- RAJU N TANNA**

SGS

SAFETY REPORT

Sr.No.	Description	Current Month	Cumulative
	A. SAFETY COMPLIANCE RECORD		
1	Percentage of First-Aid Kit Available Complete With Necessary Medicines.	100%	-
2	Percentage of Camp Labour Covered With periodic medical attention.	NA	-
3	Percentage of excavated area barricaded.	90%	-
4	Percentage of welders using Necessary PPE.	NA	-
5	Percentage of Staff & Workmen using required Safety gear.	100%	-
6	Percentage of staff & workmen getting potable drinking water.	100%	-
7	Percentage of area lighting for night work.	70%	-
	B. TRAINING AND AWARENESS PROGRAMMES CONDUCTED		
8	Total Manpower(engaged Daily average).	72	-
9	No of personnel exposed to Tool box Training (Each TBT).	72	-
10	No. of Tool box meeting held.	2	9
11	No. of safety Training Programs Conducted (October- 2013).	0	0
	C. HEALTH CHECK UP PROGRAMMES CONDUCTED		
12	No. of personal treated for minor injuries.	0	0
13	No. of personal treated for major injuries.	0	0
14	No. of personal treated for first aid.	0	2

Prepared By:- AMIT S PAWAR **Approved By:- RAJU N TANNA**

SGS

DRAWING UPDATES

Sr.No.	Drawing Details	Status	Remarks
1	Architectural Drwaings	All Levels GFC drawings issued.	UGWT revised drg. Received.
2	Structural Drawings	All Levels GFC drawings issued.	Except PT area
3	PHE Drawings	All Levels GFC drawings issued.	
4	Electrical Drawings	All Levels GFC drawings issued.	Uptill 2nd Floor
5	HVAC Drawings	All Levels GFC drawings issued.	

DRAWING RECEIPT DETAILS OCTOBER 2013

Sr.No.	Drawing No.	Title of Drawing	Issued on	No of copies	Revision
SERVICES (ELECTRICAL)					
-	-	-	-	-	-
-	-	-	-	-	-
STRUCTURAL (CIVIL)					
1	Column Footing Details	9219-1-R13	30.10.13	5	R13
2	Typical Lintel Chajja, Loft, Coping Band Beam Details.	9219-TY LINTEL	30.10.13	5	R0
3	Column Link Details	9219-1LK-R1	30.10.13	5	R1
ARCHITECTURAL (CIVIL)					
1	B1-A-7001	UGWT DETAILS	09.10.13	5	R1
PHE DRAWINGS					
1	B1-P-6005A	Flushing Water Supply SLD	28.10.13	5	R0
2	B1-P-6005B	Domestic Water Supply SLD	28.10.13	5	R0
3	B1-P-6005C	Pump Room Details	28.10.13	5	R0

Prepared By:- **AMIT S. PAWAR** **Approved By:- RAJU N TANNA**

SGS

DEPLOYMENT RECORD

LABOUR STRENGTH

Persons	Labour		Mason	Carpenter	Fitter	Machine Operator	Electrician	Welder	Plumber	Painter	Surveyor
	Male	Female									
Skilled	12	0	5	14	10	1	3	0	1	0	0
Unskilled	25	7	0	0	0	0	0	0	0	0	0

CONTRACTOR'S STAFF

Sr. No.	Designation	Required as per agreement	Deployed at site	Deficiency
1	Project Manager	1	1	-
2	Sr. Engineer (Civil)	1	1	-
3	Sr. Engineer (Electrical))	1	1	-
4	Jr. Engineer (Civil)	-	1	-
5	Jr. Engineer (Electrical)	-	-	-
6	Safety Engineer	-	-	-
7	Site Supervisor	2	2	-

PMC STAFF

Sr. No.	Designation	Required as per agreement	Deployed at site	Deficiency
1	Project Manager	1	1	-
2	Sr. Engineer (Civil)	1	1	-
3	Sr. Engineer (MEP)	1	1	-
4	Jr. Engineer (Civil)	1	1	-
5	Supervisor (MEP)	1	1	-
6	Safety Engineer	1	1	-
7	Office Assistant	1	0	1

MACHINERY & TOOLS

Sr. No.	Equipment / Machinery	Necessary as per agreement	Installed at site	Deficiency
1	Hoper mixer / Transit mixer	1	-	1
2	Building Hoist	1	0	1
3	Excavator	1	1	0
4	Vibrator	5	2	3
5	Vibrator Compactor	2	0	2
6	Dewatering Pump	2	1	1
7	Trucks	2	2	0

Prepared By:- AMIT S. PAWAR **Approved By:- RAJU N TANNA**

SGS

MATERIAL PROCUREMENT DETAILS

SR NO.	Description	Make	Qty delivered on site up to 15.10.13	Remarks
1	8mm dia - Fe500D steel bars (MT)	MITC	25.00	-
2	10mm dia - Fe500D steel bars (MT)	MITC	23.74	-
3	12mm dia - Fe500D steel bars (MT)	MITC	24.92	-
4	16mm dia - Fe500D steel bars (MT)	MITC	38.98	-
5	20mm dia - Fe500D steel bars (MT)	MITC	0.00	-
6	25mm dia - Fe500D steel bars (MT)	MITC	25.00	-
7	32mm dia - Fe500D steel bars (MT)	MITC	11.60	-
	TOTAL (MT)		**149.24**	
8	M:15 (cum)	Godrej & Boyce	163.25	Theorotical quantity may vary from actual reciept on site.
9	M:25 (cum)	Godrej & Boyce	712.50	
10	M:40 (cum)	Godrej & Boyce	79.50	
11	**TOTAL (cu.m)**		**955.25**	
12	Shahabad Tiles	-	200 sq.m	For Lift water proofing
13	Water Proofing chemical	Dr. Fixit (Pidiproof LW+)	20 litres	"
14	Bricks 3"	KBK	4526 Nos.	For Plinth Works
15	-	-	-	-
16	-	-	-	-
17	-	-	-	-
18	-	-	-	-
19	-	-	-	-
20	-	-	-	-

Prepared By: AMIT S. PAWAR **Approved by: RAJU N TANNA**

PROJECT DIRECTORY

Name	Company Name & Address	Function	Email	Mobile No.	Landline	Fax No.	Mailing	Remark
Client : IITB, Mumbai								
Mr. N Venkatramani	IIT-B Powai	Honourable Dean (IPS)	dean.ips@iitb.ac.in	-	(022)25767080	(022)25764080	Escalation 2	CC only important mails
Mr. Kiran Wagh		CACI	ks_wagh@iitb.ac.in	-			Escalation 1	CC only important mails
Mr. Milind Gokhale		OSD	mygokhale@gmail.com	9322246682			Addressee	To
SGS India Pvt Ltd - Project Management Consultant								
Mr. Sumit Singhal	SGS India Private Limited 5th Floor, Nitco Business Park, Behind Bradma, Road No 16, Wagle Industrial Estate, Thane West, Mumbai-400604, India.	National Operations Manager -	sumit.singhal@sgs.com	9004494153	(022)61870106	(022) 61870347	Escalation 2	CC only important mails
Mr. Yuvraj Galande		Assistant Manager - Industrial Services	yuvraj.galande@sgs.com	9004680288	(022)61870154	(022) 61870347	Escalation 1	cc
Mr. Raju Tanna		Project Manager	raju.tanna@sgs.com	9821673677			Addressee	To
Mr. Rakesh Merwade		Project Co-ordinator	rakesh.merwade@sgs.com	9922778855	-	-	-	-
Mr. Satish Jadhav		Senior Civil Engr.	-	9930794679	-	-	-	-
Mr. Amit Pawar		Junior Civil Engr.	-	9967882238	-	-	-	-
Mr. Oves Ahmed		Senior MEP Engineer	-	9892563393	-	-	-	-
Mr. Arun Mishra		Supervisor MEP	-	9223539342	-	-	-	-
Mr. Asutosh Tiwari		Safety Officer	-	9004219349	-	-	-	-
Architect								
Mr. Vinayak Thorat	Venkataramanan Associates, "VEDUS", First floor,Plot No.52, Sr No. 39/1.Bharatkunj Co-op Hsg. Society No.II.Behind New Abhinav School,Erandwana, Pune - 411 038 INDIA.	Branch Head	vinayak@vagroup.com	98220 33657	020 41497502	91 20 2546 1232	Escalation-1	cc
Ms.Namrata Phulgirkar		Senior Architect	namrata.phulgirkar@vagroup.com	9657595482	020 41497510		-	-
Mr. Pritam Wagh		Senior Design Manager	pritam@vagroup.com	98904 12454	020 41497514		Addressee	To
Mr.Rahul Chavan		Sr. Engg. - Services coordination	rahul.chavan@vagroup.com	99 224 55371	020 41497518		Escalation-3	cc
Mr.Sadik Khan		Team Lead - QS	sadik.khan@vagroup.com	9326843816	020 41497511		-	-
Mr.Santosh Waikar (Civil)		Senior Engineer - QS	santosh.waikar@vagroup.com	9272175114	020 41497511		Escalation-2	cc
Mr.SAMBHAJI TAPKIR (Interior)		Senior Engineer - QS	sambhaji.tapkir@vagroup.com	9552637470	020 41497508		-	-
Mr.Ahmed Nardekar (Interior)		Senior Engineer - QS	nardekar.d@vagroup.com	9272175114	020 41497508		-	-
Ms.Kavitha Menon		Interior Architect	kavitha.menon@vagroup.com	9623722064	020 41497522		Escalation-4	cc
Mr. Bhaskar Mittha		Architectural Assistant	bhaskar.mittha@vagroup.com	9730392855	020 41497510		-	-
Ms.Kojagiri Gurjar		Architect	kojagiri.g@vagroup.com	9422513810	020 41497511		-	-

PROJECT DIRECTORY

Name	Company Name & Address	Function	Email	Mobile No.	Landline	Fax No.	Mailing	Remark
Client : IITB, Mumbai								
RCC Consultant								
Mr. Jayant Inamdar	Strudcom Consultants Pvt.Ltd. Kishori Park, Flat No. 19, 20 Erandwane, Pune	MD - SCPL	jayant.inamdar@strudcom.com	NA	020-25438847	020-25438847	Escalation-1	CC only important mails
			jvinamdar@strudcom.com	NA	020-25432172	020-25432172	Escalation-1	CC only important mails
Mr. Yogesh Bang		Chief Design Engineer	yogesh.bang@strudcom.com	NA	-"-	-"-	Addressee	To
PHE Consultant								
Mr. Dheeraj Oswal	Ace Consultants (PHE & FP Consu ltants) Office No.2, Omkar Apartment,117/118, Madhav Baug Society,Shivtirthanagar, Pune 411038	Principal PHE Consultant	nileshgandhi@vsnl.net	97678 41702	020 25286273	020 2528 6273	Addressee	To
Electrical Consultant								
Mr. Nitin Nagale	Abhiyanta Electrical Consultants & Engineers, Shree Swami Krupa, Plot No. 6,Neelkamal Housing Society, Near Rajaram Bridge,Karvenagar, Pune - 411 052,Maharashtra (India)	Principal Electrical Consultant	abhiyanta@vsnl.net	98229 81483	020 25462173	020 2541 0691	Addressee	To
HVAC Consultant								
Mr. Amit	R S Kulkarni Fellow & Life Member - ASHRAE , HVACR Consultant, Office No. 512 + 513, Siddharth Towers, Sangam Press Road, Kothrud, Pune 411 029	Principal HVAC consultant	ravindrask@hathway.com	98909 69271	020 2544 60 14 / 2546 59 20	020 - 2543 6684	Addressee	To

SGS

PROGRESS PHOTOS OCTOBER 2013



Pic-1 Plinth Beam works in progress.



Pic-2 Plinth BeamCasting in progress.



Pic-3 U G Tank Plum concrete shuttering.



Pic-4 Plinth Beam PCC & shuttering in progress.



Pic-5 Plinth Beam PCC work in progress.



Pic-6 Lift wall box type water proofing done.



Pic-7 Column Footings casting completed.



Pic-8 Lift 2 Water proofing done, backfilling in progress.

Prepared By- Amit Pawar

Approved By- R N Tanna

SGS

PROGRESS PHOTOS OCTOBER 2013



Pic-9 UG Tank Plum Concrete complete & water proofing base coat done.



Pic-10 UG Tank Plum Concrete complete & water proofing base coat done.



Pic-11 Plinth Beam deshuttering done, curing in progress.



Pic-12 Plinth Beam deshuttering done, curing in progress.

Prepared By- Amit Pawar

Approved By- R N Tanna

END OF REPORT



THANK YOU
