

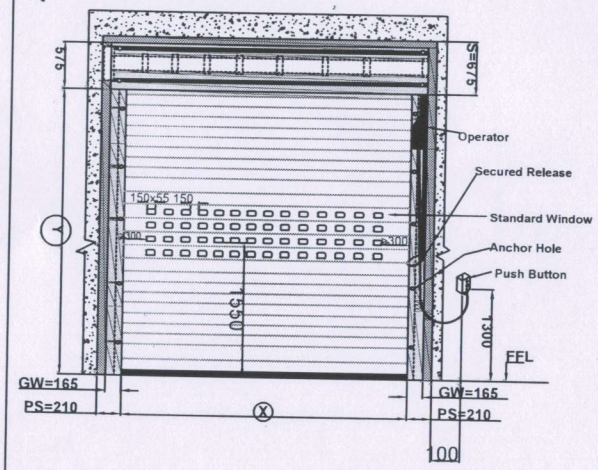


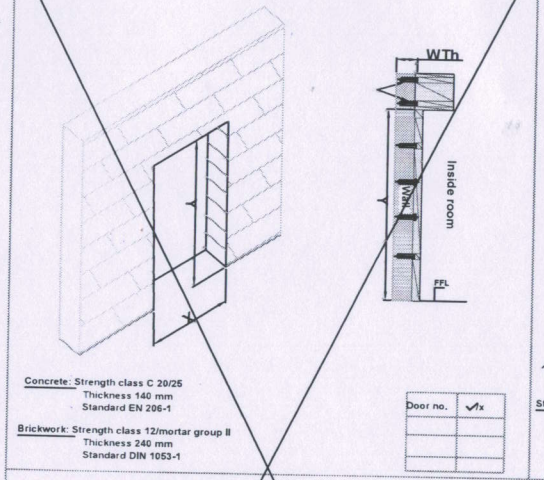


Door no.	✓x

FIXING ON BRICK WALL/CONCRETE

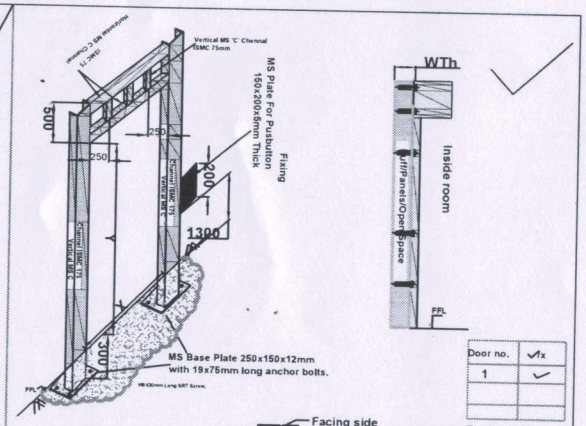


Door no.	✓x
1	✓


FIXING ON STEEL STRUCTURE



SECTION DETAIL'S




SECTION DETAIL'S
'A'A'



GW = Guide Width
ET = Min. fitting depth
S = Required Head room.
PS = Side space for cover removal & maintenance purpose

* Number of Windows Depends as per Clear Width(As per SHPL Standard)

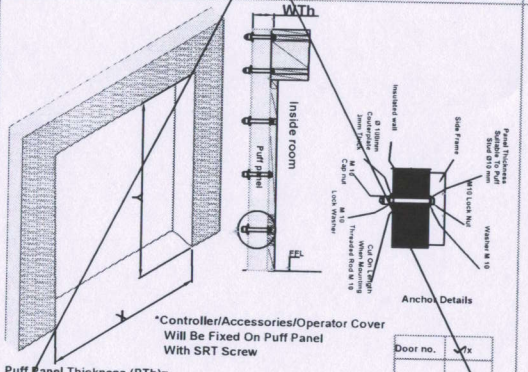

Puff Panel Thickness (PTh)=_____

Puff Panel Colour RAL _____

Door no.	✓x

FIXING ON PUFF PANELS

Client scope

1) 16A 3 Pin Industrial type female socket Modal No:-
230V, 50Hz, with earth around 1/2 Meter From Controller/Operator
2) Clean Uninterrupted Power Supply WithOut Voltage Fluctuations Needed
3) Solid State Inline (UPS/Stabilizer) 2kva Capacity Required

Notes:
1) Operator is Always on Right side as Standard
2) Push Button is Always On Operator Side
3) Steel Structure Procurement,Fixing and Strength is Client Responsibility (Minimum Dimensions are Shown in the Drawings)
4) Puff Panel Anchor bolt Length Would Change as based on Panel Thickness
5)Please Put ` `Mark For Applicoble `X` If Not Required
6)For vision Panel Locations Follow The Brochure Standes Only

Door no.	Clear X-width	Clear Y-Height	Qty.s	Motor side R or L	Colour RAL 9002
1	5000	3560	1	R	9002
2					
3					
4					
Total			1	R	9002

STANDAD ACCESSORIES:

1	Push button DTHR	1 No Per Door

OPTIONAL ACCESSORIES:

	YES/NO
Surface Mounted Push button	
Controller 360	NO

NIHVA TECHNOLOGIES PUNE PVT.LTD.

10/10/2020

Note:All Doors To Be Fixed From The Inside Only

HÖRMANN	DRAWN BY: H K CHECKED BY:T.R.B APPROVED BY: Babu Sir
TITLE:ROLLING SHUTTER-SB(SPRING BALANCE) WITH STANDARD WINDOW	DRAWING NOT TO SCALE
CLIENT:M/s. Nihva Technologies	D R G. N O. 9314 REV 0
PROJECT:M/s. Nihva Technologies	Ref : Teams DATE: 05-10-2020
