

1. Shimizu Approved.
2. Please proceed fabrication.


DOCK LEVELER SIZE	WIDTH (W)	LENGTH (L)	HEIGHT (H)	LIP (C) LENGTH
	2250	3200	480	400


PIT DIMENSION	WIDTH (W 1)	LENGTH (L 1)	DEPTH (D)	ALL DIMENSIONS ARE IN mm
	2300	3270	485	

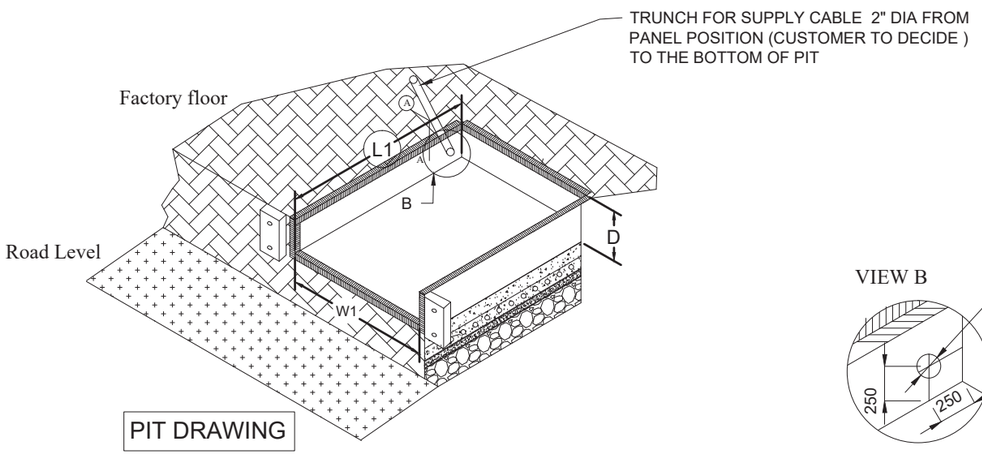


PIT DRAWING



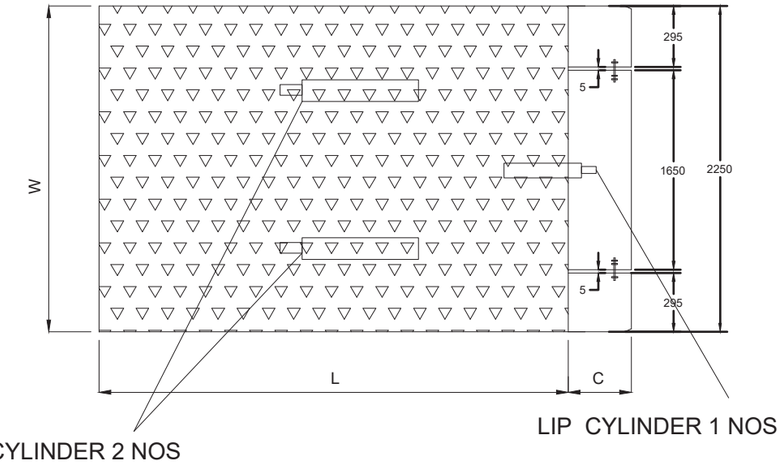



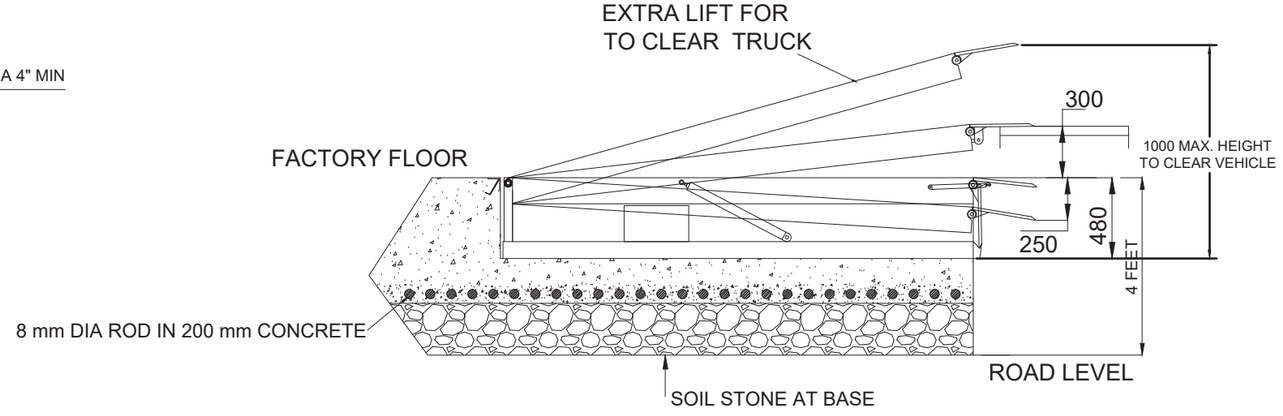

DOCK LEVELER- 6 TON CAPACITY

NOTE: -
1. PROPER DRAINAGE SHOULD BE DONE
2. TRENCH AS SHOWN SHOULD BE MADE BY DECIDING THE POWER PACK POSITION (SUPPLY CABLE LENGTH STD. 7000 MM)
3. LEVEL OF THE PIT SHOULD BE PLAIN AND SHOULD TAKE AT LEAST 10000 KG FLOOR LOADING
4. MOUNTING ARRANGEMENT FOR BUFFERS SHOULD BE MADE AS PER BUFFER DRAWING (IF ORDERED)
5. FABRICATION TOLERANCE FOR PLATFROM SIZE WILL BE ± 15 MM

CLIENT APPORVAL-	DATE	SIGN.
DRAWN :- SURAJ	28/06/2017	
CHECKED:- SHEKHAR.	28/06/2017	
APPROVED:-SHEKHAR.	28/06/2017	
ALL DIMENSION ARE IN mm		
If any queries contact : projects@nihva.com		

NIHVA TECHNOLOGIES PVT. LTD.
NIHVA TECHNOLOGIES PVT. LTD. PUNE
Tel : 020 66304033
Email:- info@nihva.com
Website:- www.nihva.com

CLIENT - SIMZU CORPORATION INDIA PVT. LTD.
PROJECT -TRMN EXPNSION FACTORY
SITE -BANGALORE.
DWG. NO. - NIHVA/17-18/0242
